

SOFTWARE ENGINEERING LAB2


NAME: SRINIDHI P

SRN: PES1UG24AM407


SECTION:G

OUTPUT SCREENSHOTS :


1.(EPICS)

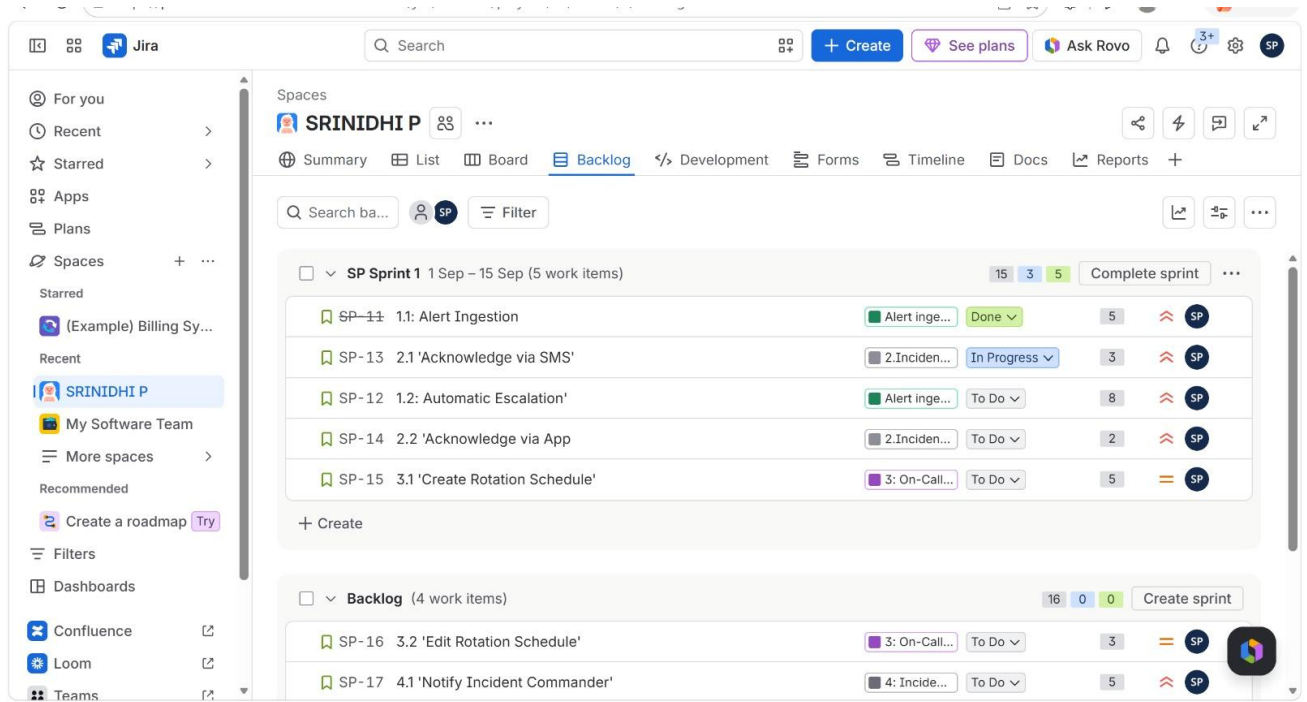


2.

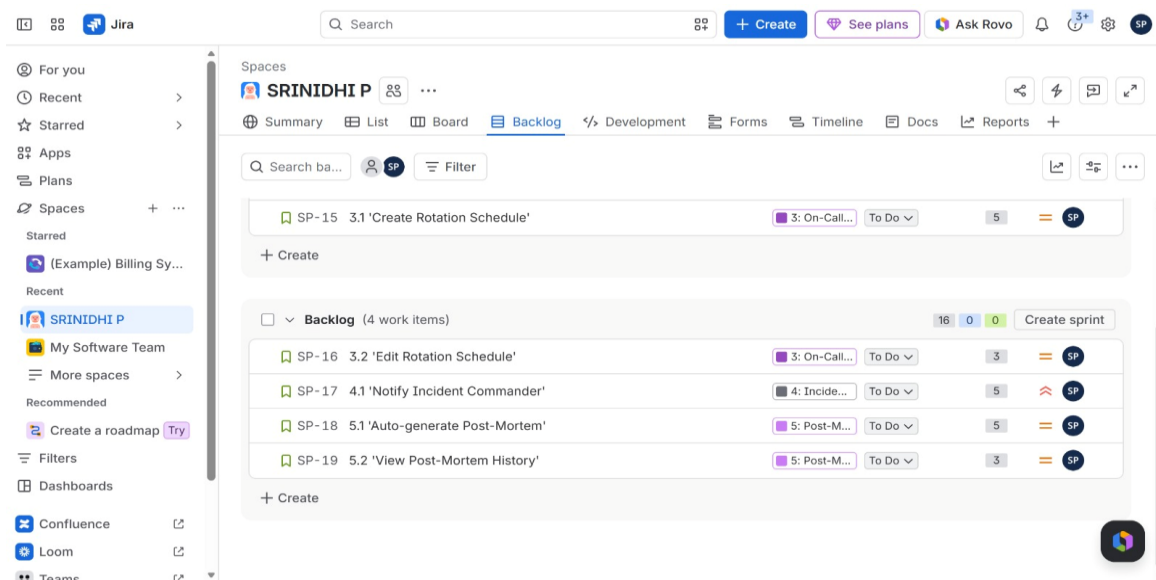


3.

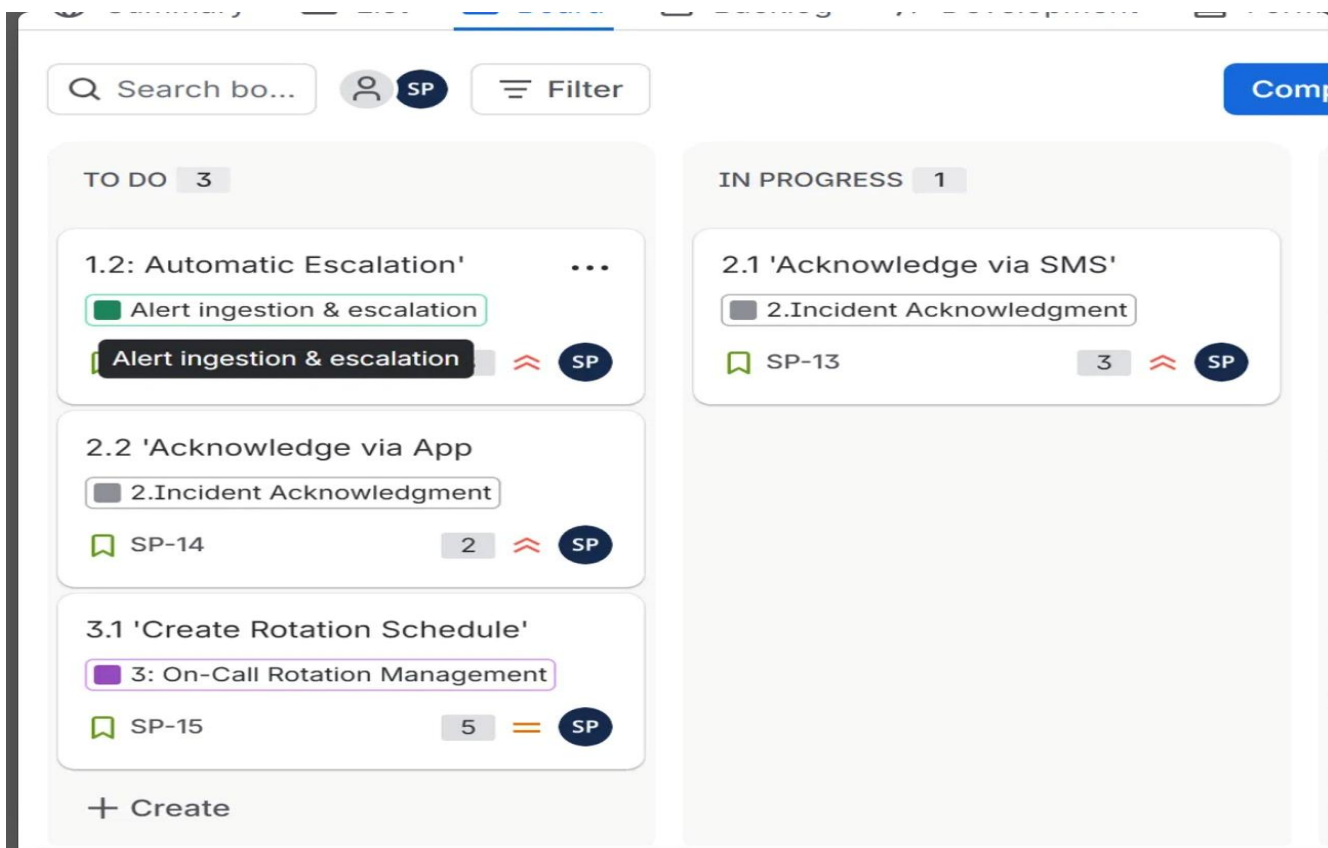

4.

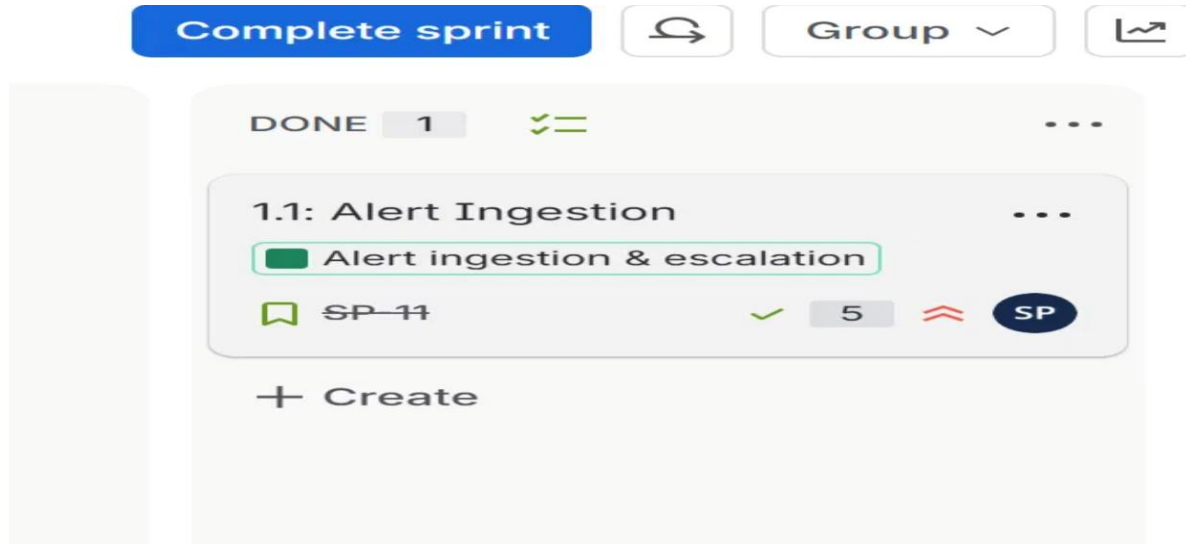

5.

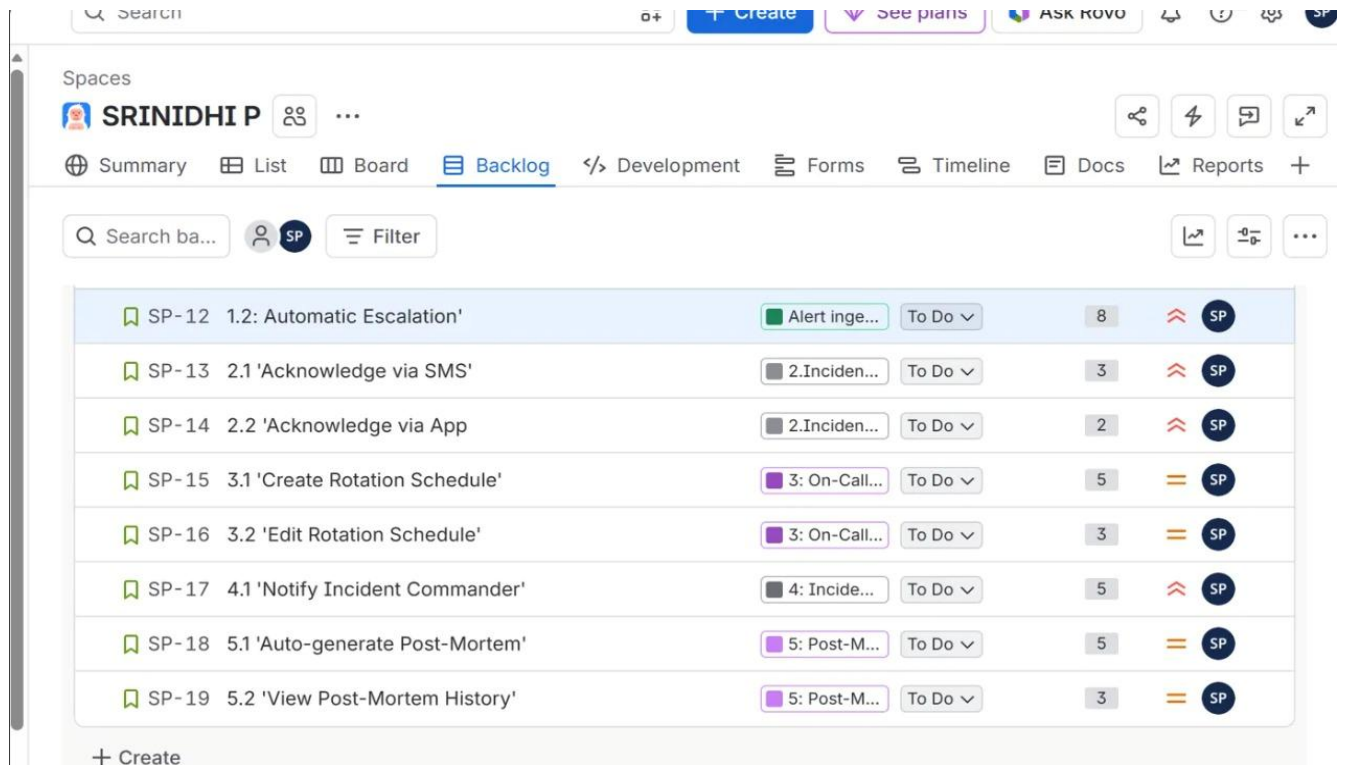

6.(BURNUP REPORT)


Sprint

SP Sprint 1

Estimation field


Story points

Date - September 1st, 2026 - September 15th, 2026

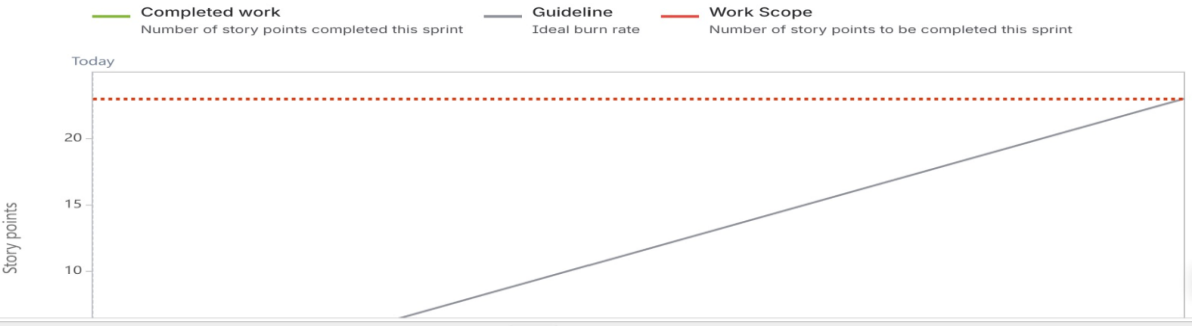

7.

Date - September 1st, 2026 - September 15th, 2026

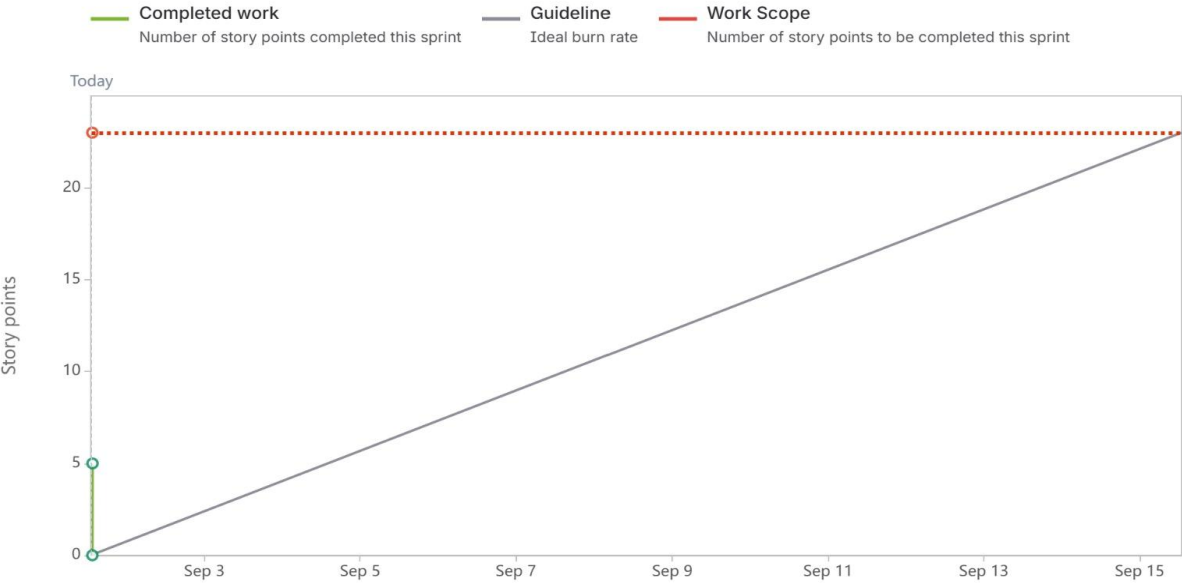

8.

Date				
Date	Event	Work item	Completed	Scope
Tue, Sep 01 2026, 12:59pm	Sprint started	SP-13 2.1 'Acknowledge via SMS' SP-11 1.1: Alert Ingestion SP-12 1.2: Automatic Escalation' SP-15 3.1 'Create Rotation Schedule' SP-14 2.2 'Acknowledge via App'	0	23
Tue, Sep 01 2026, 1:02pm	Work item completed	SP-11 1.1: Alert Ingestion	0 → 5	23

9.(OPTIONAL EPICS)

Jira

Search

+ Create

See plans

Ask Rovo

3+

For you

Recent

Starred

Apps

Plans

Spaces

Starred

(Example) Billing Sy...

Recent

SRINIDHI P

My Software Team

More spaces

Recommended

Create a roadmap

Try

Filters

Dashboards

Confluence

Loom

Spaces

SRINIDHI P

Summary

List

Board

Backlog

Development

Forms

Timeline

Docs

Reports

Search bo...

SP

Filter

Complete sprint

Group

TO DO

4

3.2 'Edit Rotation Schedule'

3: On-Call Rotation Management

SP-16

3

SP

5.1 'Auto-generate Post-Mortem'

5: Post-Mortem Tracking

SP-18

5

SP

4.1 'Notify Incident Commander'

4: Incident Commander Escalation

SP-17

5

SP

IN PROGRESS

IN REVIEW

DONE

10.

5.1 'Auto-generate Post-Mortem'

5: Post-Mortem Tracking

 SP-18

5

=

SP

4.1 'Notify Incident Commander'

4: Incident Commander Escalation

 SP-17

5

>

SP

 SP-18

5

=

SP

4.1 'Notify Incident Commander'

4: Incident Commander Escalation

 SP-17

5

>

SP

5.2 'View Post-Mortem History'

5: Post-Mortem Tracking

 SP-19


3

=

SP

+ Create

11.(BURNUP REPORT)

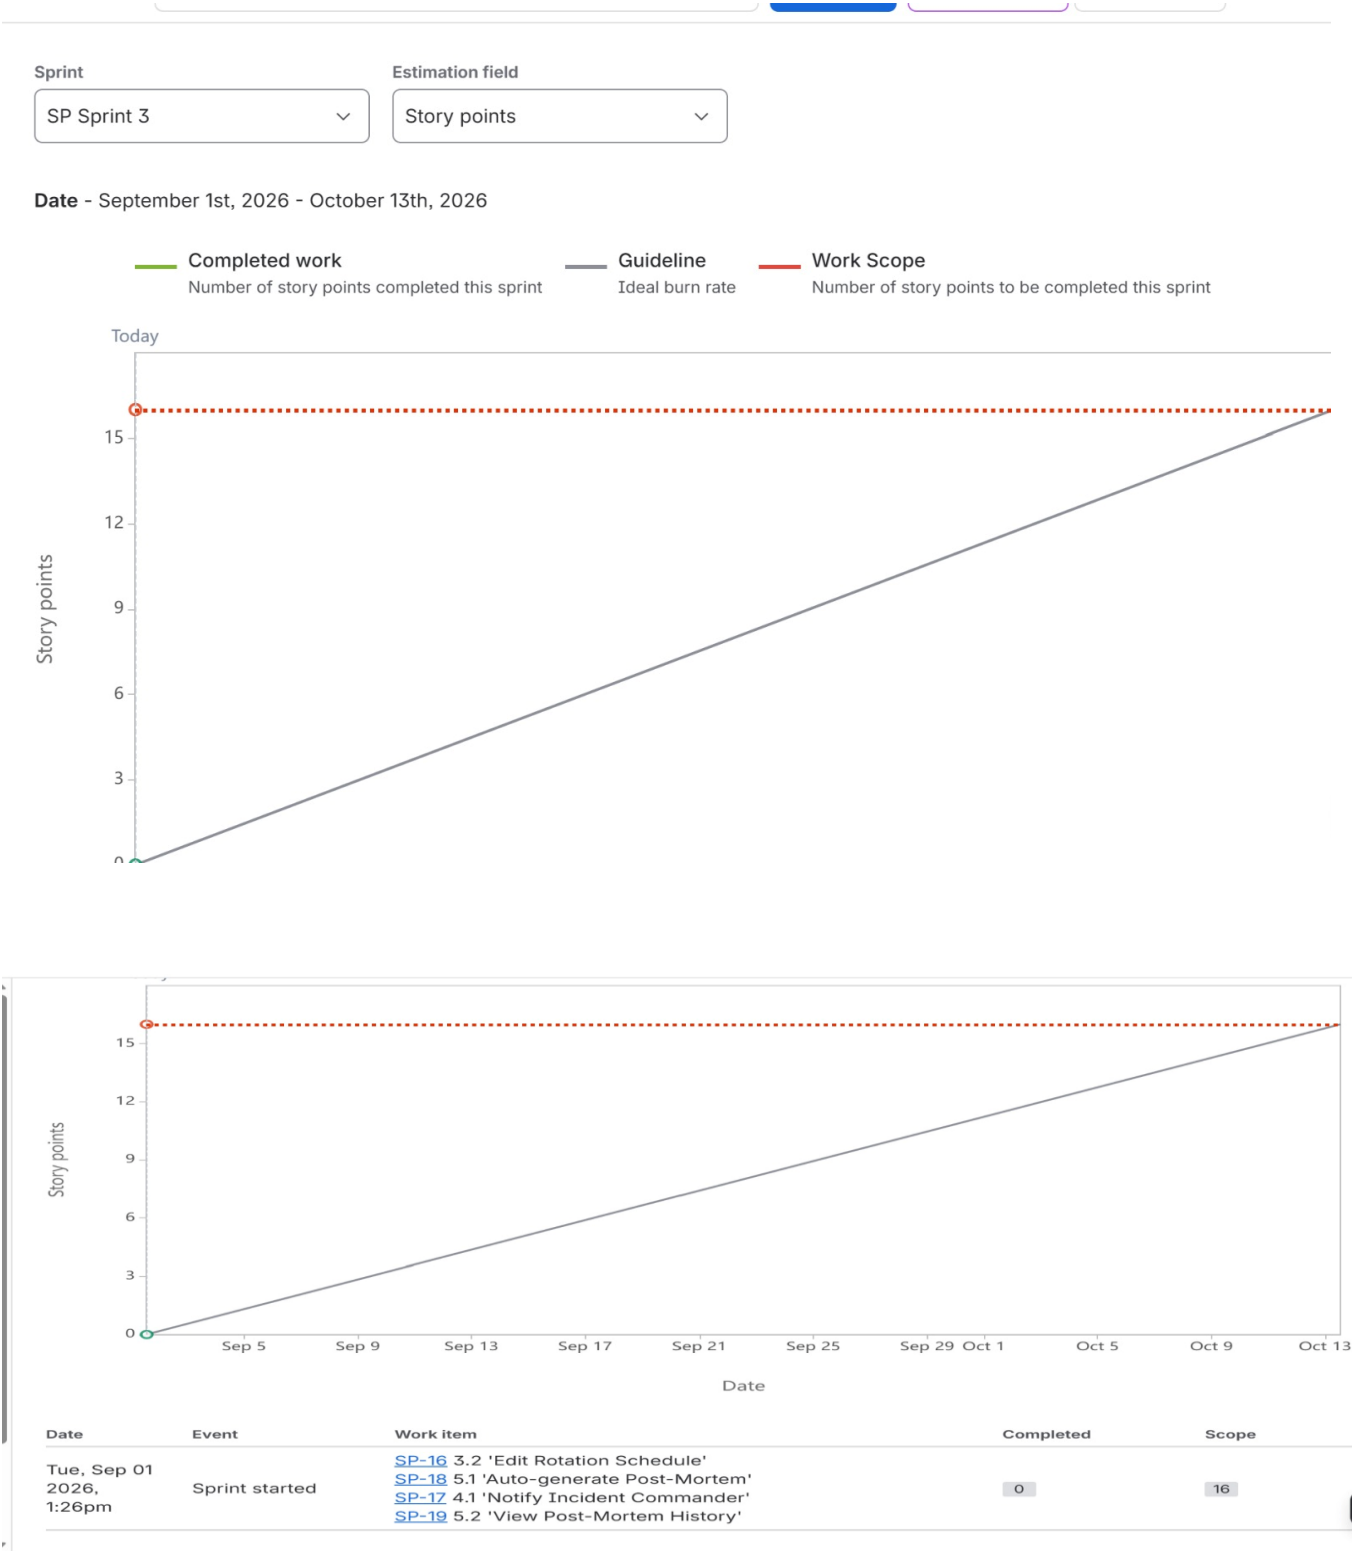

Reflection Questions:

1. Did your estimations reflect the actual effort?

Mostly yes. Story points were assigned relative to complexity rather than fixed time, so straightforward stories like "Acknowledge via App" (2 pts) were clearly smaller than multi-step stories like "Automatic Escalation" (8 pts), which involves timeout logic and routing to a secondary engineer. The relative sizing held up well, though "Automatic Escalation" arguably could have been split into smaller stories given its complexity relative to the others.

2. Was your backlog well-prioritized?

Yes, priority was assigned based on user and business impact. Stories directly affecting incident response time — alert ingestion, escalation, and acknowledgment (SP-11 to SP-14, SP-17) — were marked High since delays here directly risk missed incidents. Supporting and administrative stories like editing rotation schedules and viewing post-mortem history (SP-15, SP-16, SP-18, SP-19) were marked Medium since they don't block active incident handling.

3. How did your simulated sprint align with your plan?

Sprint 1 planned for 5 stories totaling 23 story points. By the time of the mid-sprint check, 1 story (5 points) was Done, 1 was In Progress, and 3 remained in To Do — roughly 22% of planned work completed. This is behind the ideal linear pace for a 1-week sprint, which is expected in a compressed lab simulation rather than a real week-long sprint.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart showed the remaining-values line sitting above the guideline line, indicating the team was behind the expected pace at that point in the sprint. In a real scenario, this would prompt re-checking whether the committed stories were realistically sized for the sprint duration, or whether work needs to be reprioritized or split further to stay on track.
